A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Bajua Bazar, Mongla, Bagerhat.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 1.82m below from Road Level.
CLIENT : Grameenphone Ltd.	DATE OF BORING : 21-03-2008.	G. W. T : 1.52m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
7.5.0m	Gray 10YR (6/1), very soft to stiff, silty Clay, CL.		UD-1, UD-2, UD-4	D-1, D-2, D-4, D-5, D-6	1, 1, 0, 1, 1, 3		
3.0m	Light gray 10YR (7/2), stiff to very stiff, silty Clay, CL.			D-7, D-8	14, 16		
1.5m	Gray 10YR (6/1), dense to very dense, silty Sand, SM.			D-9, D-10	26, 37		
1.5m	Lihgt gray 10YR (7/2), very dense, silty Sand, SM.			D-11, D-12	40, 46		
7.95m	Gray 10YR (6/1), very dense, fine sand, SM.			D-13, D-14, D-15, D-16	48, 50, 50, 50		Over, Over, Over

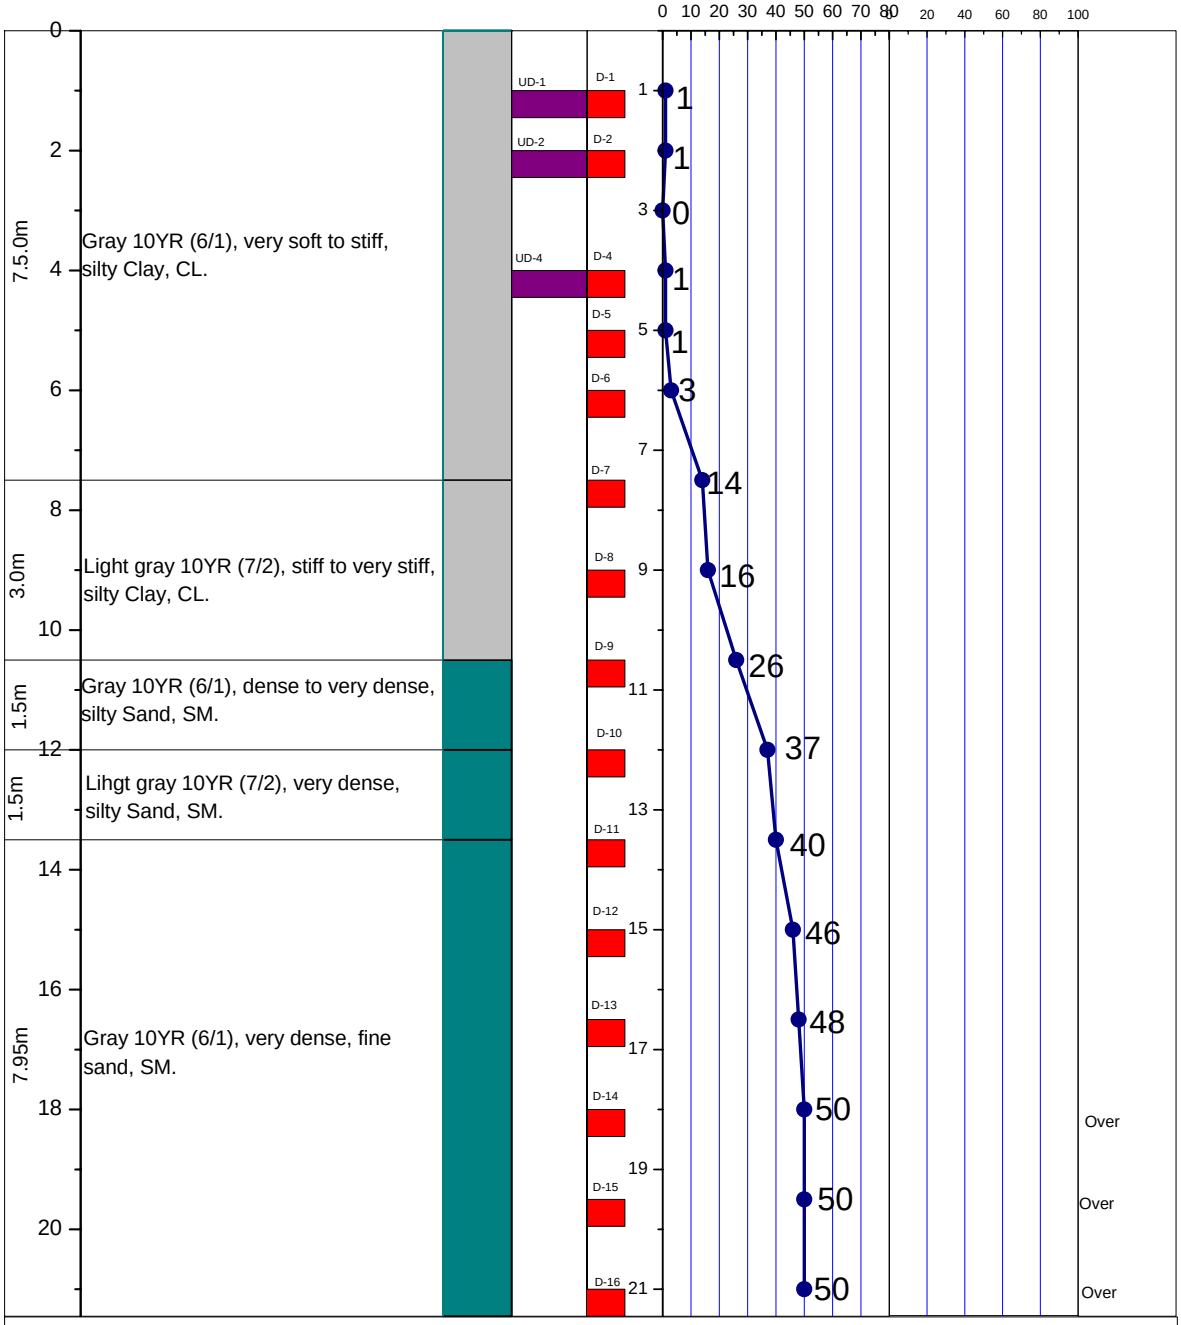

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
