A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Kamalla, Muradnagar, Comilla.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 2.29m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 04-08-2008	G. W. T : 1.06m above from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
2.0m	Light gray 10YR (7/1), very loose to medium dense, silty Sand, SM.			D-1 to D-2	1, 9		
6.0m	Gray 10YR (6/1), medium dense to loose, fine sand, SM.			D-3 to D-7	4, 2, 10, 11, 6		
1.0m	Yellow 10YR (7/6), loose to medium dense, silty Sand, SM.			D-8 to D-9	5, 7		
4.5m	Gray 10YR (6/1), medium dense to very dense, fine sand, SM.			D-10 to D-12	7, 16, 37		
7.95m	Light gray 10YR (5/1), very dense, fine sand, SM.			D-13 to D-17	40, 41, 42, 45, 44		

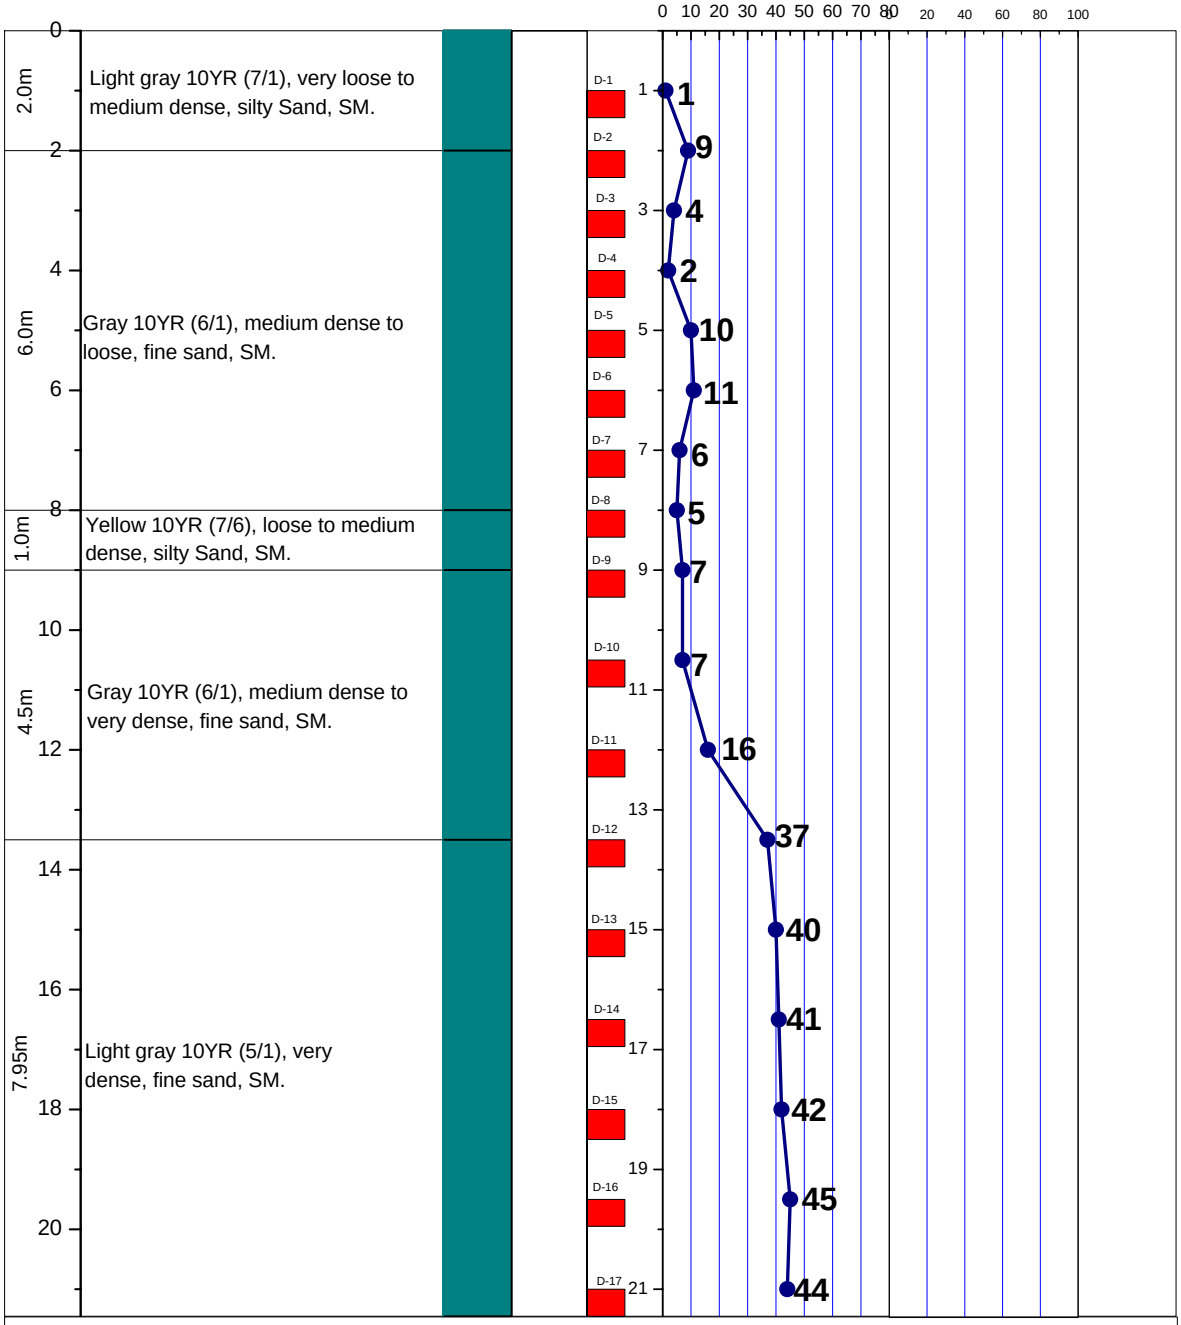

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
