A2 PROSOIL	BOREHOLE NO: BH-1	
	LOCATION : Comilla University, Salmanpur, Comilla.	
PROJECT : Telecommunication Tower.	DEPTH OF BORING : 21.0m	R. L.: 0.17m below from Road Level.
CLIENT : TM International, Bangladesh Ltd.	DATE OF BORING : 24-01-2009	G. W. T : 3.35m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
5.0m	Reddish brown 5YR (5/3), medium dense to loose, cohesionless silt, SM.			D-1 to D-5	7, 8, 7, 4, 5		
1.0m	Light reddish brown 5YR (6/4), loose, cohesionless silt, SM.			D-6	6		
4.5m	Brown 7.5YR (5/4), loose to dense, fine sand, SM.			D-7 to D-9	10, 12, 17		
10.95m	Light brown 7.5YR (6/4), dense to very dense, fine sand, SM.			D-10 to D-17	23, 30, 37, 44, 48, 50, 50, 50		over, over, over

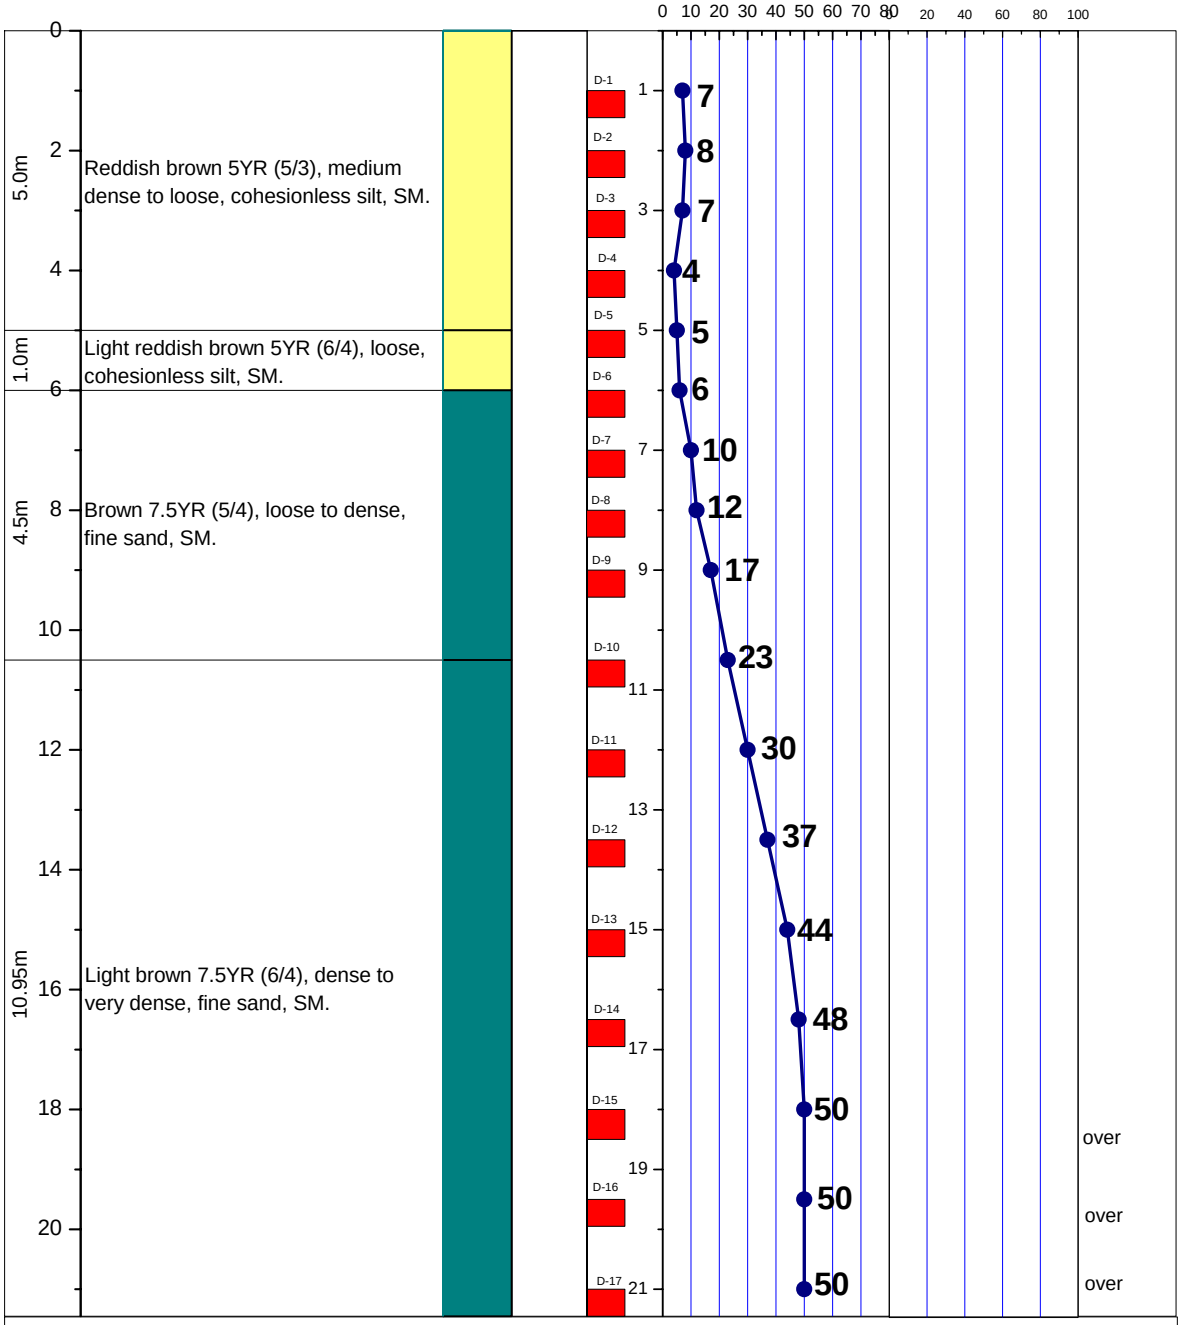

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION

PLASTIC SILTY CLAY

LOW PLASTIC CLAYEY SILT

NON PLASTIC SILT

SAND

ORGANIC

UNDISTURBED SAMPLE

DISTURBED SAMPLE

SHALE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
