A2	PROSOIL	BOREHOLE NO: BH-1	
		LOCATION: Fulgor (Purbadhair), Muradnagor, Comilla	
PROJECT : Telecommunication Tower.		DEPTH OF BORING: 21.0m	R. L.: 0.76m above from Road Level.
CLIENT : AXIATA (Bangladesh) Ltd.		DATE OF BORING: 22-09-2010.	G. W. T : 2.13m below from E. G. L.

THICKNESS	SOIL STRATA	BORELOG	UNDISTURBED SAMPLE	DISTURBED SAMPLE	DEPTH (m) SPT VALUES (BLOWS / 300mm)	Grain Size Distribution, % Clay %, Silt %, Sand %	Max^{m} Penetration
3.0m	Reddish Brown 2.5YR (5/3), medium dense to loose, Silt, ML.			D-1 to D-3	8, 4, 9		
1.0m	**Grayish Brown 10YR (7/3), medium plasticity, medium stiff to very stiff, silty Clay, CL.**		UD-3	D-3	9		
12.5m	Bluish Gray Gley2 (5/1), dense to very dense, fine Sand, SM.			D-4 to D-13	17, 16, 14, 18, 24, 35, 22, 20, 17, 18		
4.95m	Light bluish Gray Gley2 (7/1), dense to very dense, fine Sand, SM.			D-14 to D-17	30, 40, 28, 23		

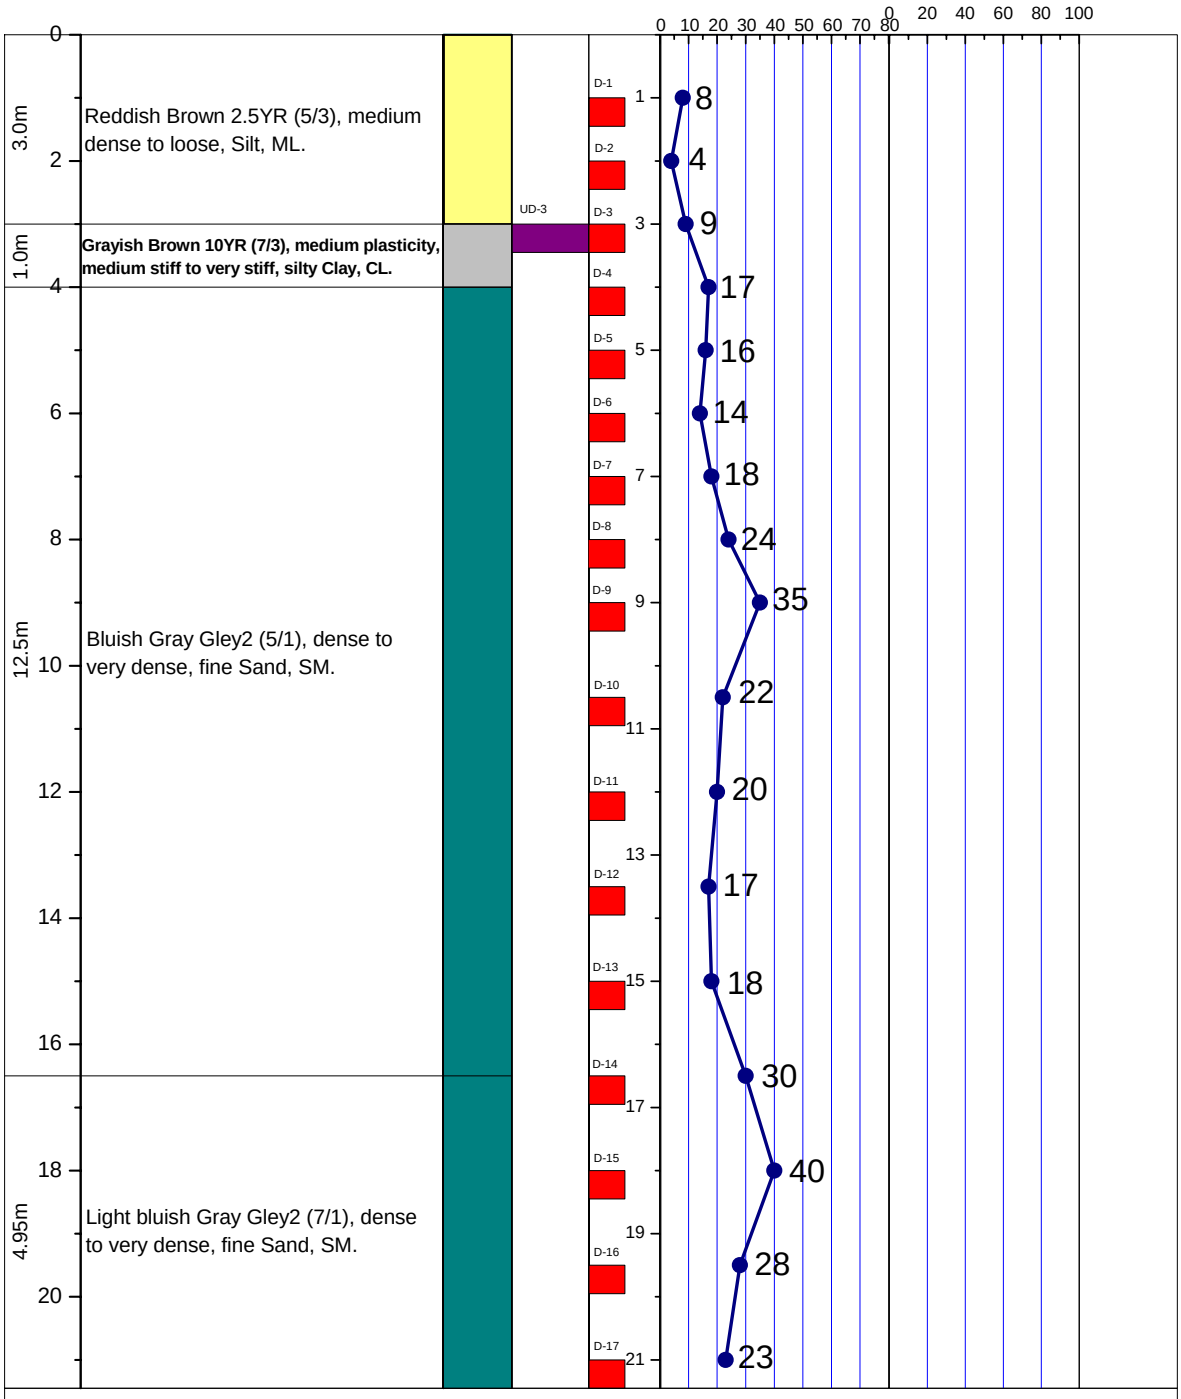

LEGEND FOR BORELOG AND GRAIN SIZE DISTRIBUTION (BASED ON 'ASTM CLASSIFICATION D-2487')

PLASTIC CLAY	SAND	SILT	SHALE
PEAT/HIGHLY ORGANIC SOIL	MICACEOUS FINE SAND/SILT	UNDISTURBED SAMPLE	DISTURBED SAMPLE

N- BLOWS DELIVERED PER FOOT BY A 140 LB HAMMER FALLING 30 INCHES

MAX^{m} PENETRATION= 50 BLOWS

AFTER 50 BLOWS PENETRATION DEPTH WERE MEASURED
